


**Chelan County
RENOVATION FOR PROSECUTOR OFFICE
OWNER'S PROJECT SCHEDULE**

Initial Date: October 25, 2009

ID	Task Name	Duration	Start	Finish	Pred.	Resource Names	4th Quarter					1st Quarter			2nd Quarter	
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1	PROJECT START	0 days	Tue 9/1/09	Tue 9/1/09												
2																
3	DESIGN	42.5 days?	Tue 9/1/09	Wed 10/28/09												
4	Design Period	35 days	Tue 9/1/09	Mon 10/19/09	1	MJ Neal										
5	Design Completion	0 days	Mon 10/19/09	Mon 10/19/09	4	MJ Neal										
6	Schedule Development	1 day?	Tue 10/20/09	Tue 10/20/09	5	RKA										
7	Division "0" Development	1 day	Sun 10/25/09	Sun 10/25/09	6	RKA										
8	Final Document Coordination	0.5 days?	Mon 10/26/09	Mon 10/26/09	7	RKA,DuLac										
9	Bid Document Finalization and submittal for BOC Packet	2 days	Mon 10/26/09	Wed 10/28/09	8	RKA										
10																
11	BIDDING AND AWARD	26 days	Mon 11/2/09	Tue 12/8/09												
12	<i>BOC Meeting - Authorization to Bid</i>	0 days	Mon 11/2/09	Mon 11/2/09	9	BOC										
13	Submit Advertisement	1 day	Mon 11/2/09	Mon 11/2/09	12	RKA										
14	First Advertisement	1 day	Wed 11/4/09	Wed 11/4/09	13											
15	Second Advertisement	1 day	Wed 11/11/09	Wed 11/11/09	14											
16	Release Documents	1 day	Wed 11/4/09	Wed 11/4/09	14FF	DuLac										
17	Bidding Period	15 days	Wed 11/4/09	Tue 11/24/09	16SS											
18	Proposal Due Date - 9:00 AM BID OPENING	0 days	Tue 11/24/09	Tue 11/24/09	17	BOC										
19	Review Bids, Finalize Agreeemnt, NIA, Recommendation to BOC and Submit for Board Packet	2 days	Wed 11/25/09	Thu 11/26/09	18	RKA										
20	<i>BOC Meeting - Action toward Award and issue NIA</i>	0 days	Mon 11/30/09	Mon 11/30/09	19											
21	Contractor Pre-Contract Submittals and Review	6 days	Mon 11/30/09	Mon 12/7/09	20	RKA										
22	<i>BOC Meeting - Action on Agreement</i>	0 days	Tue 12/8/09	Tue 12/8/09	21											
23																
24	CONSTRUCTION	77 days	Wed 12/9/09	Thu 3/25/10												
25	Pre-Construction Meeting and Issue NTP	0 days	Wed 12/9/09	Wed 12/9/09	22											
26	Construction Period - 45 Calendar Days	33 days	Wed 12/9/09	Fri 1/22/10	25											
27	Substantial Completion	0 days	Fri 1/22/10	Fri 1/22/10	26											
28	Contractor Completion - Substantial to Final Completion - 10 Calendar Days	9 days	Mon 1/25/10	Thu 2/4/10	27											
29	Final Completion	0 days	Thu 2/4/10	Thu 2/4/10	28											
30	Write Recommendation to BOC for Final Acceptance	1 day	Fri 2/5/10	Fri 2/5/10	29											
31	<i>BOC Meeting - Action on Final Acceptacne</i>	0 days	Mon 2/8/10	Mon 2/8/10	30											
32	Retainage Period - 45 Calendar Days	34 days	Mon 2/8/10	Thu 3/25/10	31											
33	Retainage Release	0 days	Thu 3/25/10	Thu 3/25/10	32											

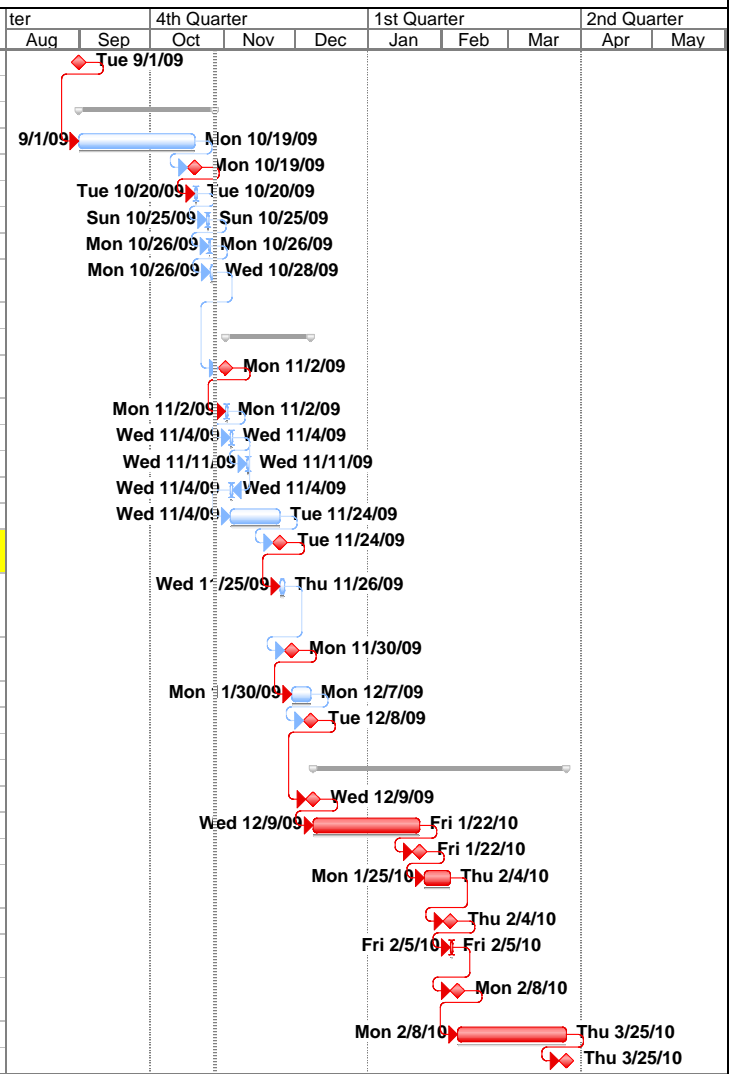

Project: CCO - PROSECUTORS OFFI Date: Wed 10/28/09	Task		Milestone		Rolled Up Critical Task		Split	
	Critical Task		Summary		Rolled Up Milestone		Deadline	
	Progress		Rolled Up Task		Rolled Up Progress			
